City of Livingston Downtown Alley CIP

ID	Task Mode	Task Name	Duration	Start	Finish	% Complete
1		**City of Livingston Downtown Alley CIP**	**160 days**	**Fri 4/4/25**	**Thu 11/13/25**	**4%**
2		**Preconstruction**	**51 days**	**Fri 4/4/25**	**Fri 6/13/25**	**13%**
3		Notice of Award	1 day	Fri 4/4/25	Fri 4/4/25	100%
4		SWPPP	16 days	Mon 4/7/25	Mon 4/28/25	0%
5		Submittals	25 days	Mon 4/7/25	Tue 6/3/25	30%
6		Pre-Construction Meeting	1 day	Tue 6/3/25	Wed 6/4/25	0%
7		Mobilization	5 days	Mon 6/2/25	Fri 6/6/25	0%
8		Notice to Proceed	0 days	Mon 6/9/25	Mon 6/9/25	0%
9		Temporary Water Setup	15 days	Mon 5/26/25	Fri 6/13/25	0%
10		**Construction**	**113 days**	**Mon 6/9/25**	**Wed 11/12/25**	**0%**
11		**Sewer Main Install**	**50 days**	**Mon 6/16/25**	**Fri 8/22/25**	**0%**
12		SSMH #4 Tie to Exisiting 10" Sewer Main	2 days	Mon 6/16/25	Tue 6/17/25	0%
13		Install Sewer Main Sta.15+16 to 10+42	15 days	Wed 6/18/25	Tue 7/8/25	0%
14		Connect to Existing SSMH #3	1 day	Wed 7/9/25	Wed 7/9/25	0%
15		Install Sewer Main Sta.10+42 to 5+76	14 days	Wed 7/9/25	Mon 7/28/25	0%
16		Install New SSMH #2	4 days	Tue 7/29/25	Fri 8/1/25	0%
17		Install Sewer Main Sta.5+76 to 1+34	14 days	Tue 7/29/25	Fri 8/15/25	0%
18		Connect to Existing 10" Sewer Main @W. Callender St.	2 days	Mon 8/18/25	Tue 8/19/25	0%
19		Clean & Tv New Sewer Main. Pressure Test New SSMH's	3 days	Wed 8/20/25	Fri 8/22/25	0%
20		Sewer Completion	0 days	Fri 8/22/25	Fri 8/22/25	0%
21		**Water Main Install**	**85 days**	**Mon 6/9/25**	**Fri 10/3/25**	**0%**
22		Connect to Existing 10" Water Main West Geyser St.	3 days	Mon 8/25/25	Wed 8/27/25	0%
23		Install Water Main Sta.14+63 to 10+00	7 days	Thu 8/28/25	Fri 9/5/25	0%
24		Flush/Pressure/Chlorinate Sta.14+63 to 10+00	4 days	Mon 9/8/25	Thu 9/11/25	0%
25		Install Water Main Sta.10+00 to 5+00	7 days	Mon 9/8/25	Tue 9/16/25	0%
26		Install Water Main Sta.5+00 to 1+05	7 days	Wed 9/17/25	Thu 9/25/25	0%
27		Connect to Existing 10" Water Main Callender St	2 days	Fri 9/26/25	Mon 9/29/25	0%
28		Flush/Pressure/Chlorinate Sta.10+00 to 1+05	4 days	Tue 9/30/25	Fri 10/3/25	0%
29		Water Completion	0 days	Fri 10/3/25	Fri 10/3/25	0%
30		**Storm Drain Install**	**85 days**	**Mon 6/9/25**	**Fri 10/3/25**	**0%**
31		Install Storm Pipe & Inlets in Alley Behind Wilcoxsons	4 days	Tue 9/30/25	Fri 10/3/25	0%
32		Install Strom Drain, Manhole & Inlets on Lewis Street	3 days	Mon 6/9/25	Wed 6/11/25	0%
33		Clean & Tv Storm Drain	1 day	Thu 6/12/25	Thu 6/12/25	0%
34		Storm Drain Completion	0 days	Fri 10/3/25	Fri 10/3/25	0%
35		**Vault Fill**	**2 days**	**Thu 6/12/25**	**Fri 6/13/25**	**0%**
36		Excavate, Pour Wall, & Backfill Existing Vault	2 days	Thu 6/12/25	Fri 6/13/25	0%
37		**Asphalt & Concrete Restoration**	**41 days**	**Wed 9/17/25**	**Wed 11/12/25**	**0%**
38		Alley Surface Demo, Excavation, & Gravel	22 days	Wed 9/17/25	Thu 10/16/25	0%
39		Concrete Replacement W. Geyser & Clark Street	5 days	Wed 9/17/25	Tue 9/23/25	0%
40		Asphalt Replacement - W. Geyser to Clark Street	5 days	Wed 9/24/25	Tue 9/30/25	0%
41		Concrete Replacement W. Callender & Lewis Street	5 days	Wed 9/24/25	Tue 9/30/25	0%
42		Asphalt Replacement - Clark Street to Callender Street	18 days	Mon 10/6/25	Wed 10/29/25	0%
43		Final Cleanup	10 days	Thu 10/30/25	Wed 11/12/25	0%
44		Substantial Completion	0 days	Wed 10/29/25	Wed 10/29/25	0%
45		Final Completion	0 days	Wed 11/12/25	Wed 11/12/25	0%

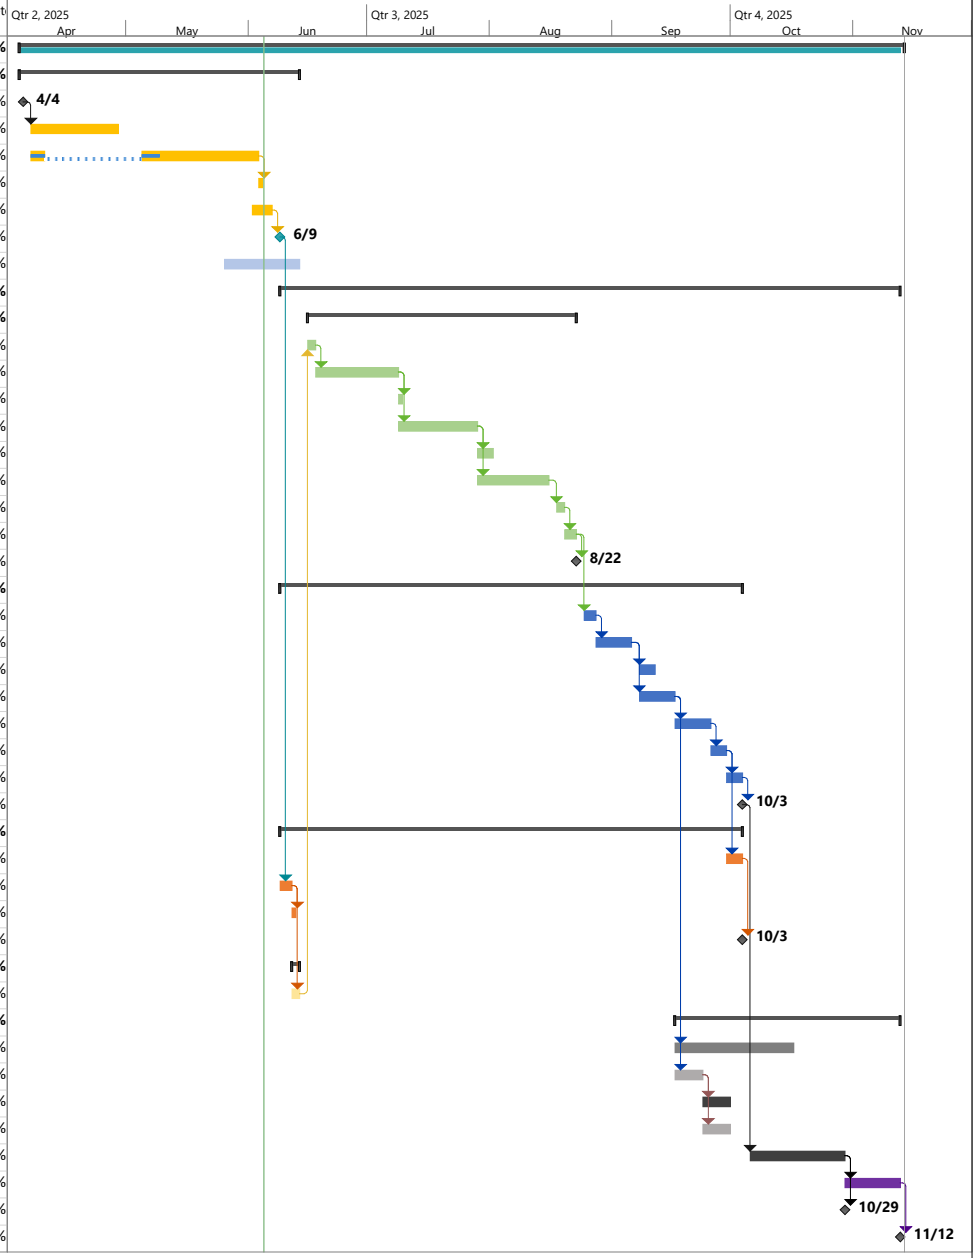

Askin Construction LLC
3300 2nd Ave. N, Suite 3
Billings, MT 59101
